Fiona: Team Roadmap and Task Plan

Oct 12, 2026 · @Ye

Every task has one owner, one finish date and a "done when" test, and the first gate is Wednesday 14 October.

Plan at a glance

The preliminary round closes on Monday 2 November, so we have 21 days: three build weeks, a feature freeze on Thursday 29 October, and a submission target of Sunday 1 November to leave one day of slack.

- **Four lanes, one owner each.** Asharib owns the platform, interface and Claude agents. Abdullah owns the finance rulebook, tests and pitch. Daniyal owns data, the ledger and the safety checks. Yahya owns forecasting, decisions and Launch Lab.
- **Five gates.** Each gate is a date on which something specific must work, so problems show up early instead of in the last week.
- **Pairs, not solo.** Every lane has a buddy who can answer questions within hours and take over a task if its owner is blocked.
- **Mock first.** Nobody waits for another lane: each module ships a fixture-backed mock by Wednesday 14 October, and real code replaces it behind the same contract.

How to use this doc. Find your section and work top to bottom: tasks are in the order to do them. Change your own status as you go, using the dropdown. If a date is wrong, comment on it instead of silently slipping; a slipped date is only a problem when the team does not know.

The companion document, *Fiona: Build Blueprint*, defines the boxes, the contracts between them and the data model. Task IDs here (A1, B1, D1, Y1) are referenced there.

Lanes and pairs

Each lane maps to a part of the product the team already described, so nobody has to learn a new area. Pairs sit on the seams where two lanes hand work to each other.

Owner	Lane	Builds	Main languages	Pair (buddy)
Asharib	Platform, interface and agents	Repo and CI, web app, Claude agent runtime, Guardian adversarial review, briefing, approvals, Guide	TypeScript, Python	Daniyal: contracts and the Guardian
Abdullah	Finance brain	Rulebook (stage rules, decision thresholds, Guardian policies), test scenarios, framework rulepack content, gold-standard memos, finance QA, pitch and video	YAML, Markdown, Excel; some Python	Yahya: rulebook becomes code
Daniyal	Data and safety	Ledger schema, synthetic data generator and answer key, importers, reconciliation, duplicate detection, Guardian deterministic checks, agent-wallet sandbox, second persona	Python, SQL	Asharib: contracts and the Guardian
Yahya	Forecasting and decisions	Stage Detector, ratios, 13-week cash forecast, debt-versus-equity and dividend calculators, inventory analytics, Launch Lab	Python	Abdullah: rulebook becomes code

Why this split

- It follows the ideas each of you brought: Abdullah's decision and control logic, Daniyal's scale and personalisation, Yahya's forecasting, and Asharib's architecture and interface.


- The two riskiest seams, contracts and the rulebook, each have two people looking at them.
- Abdullah's lane is deliberately mostly rules, tests and content, because those are what decide whether the advice is right. If Abdullah also codes, he takes Y2 (Stage Detector and ratios) from Yahya and Yahya takes more of the Launch Lab.

Pair rule. If anyone has been blocked for more than a day, the buddy is told the same day. The buddy can take over any task in that lane, so no single absence stops the build.

Timeline

Four lanes converge on five gates, with one day of slack before the deadline

Weekly ticks; each bar is that lane's focus for the week, and the task tables hold the detail

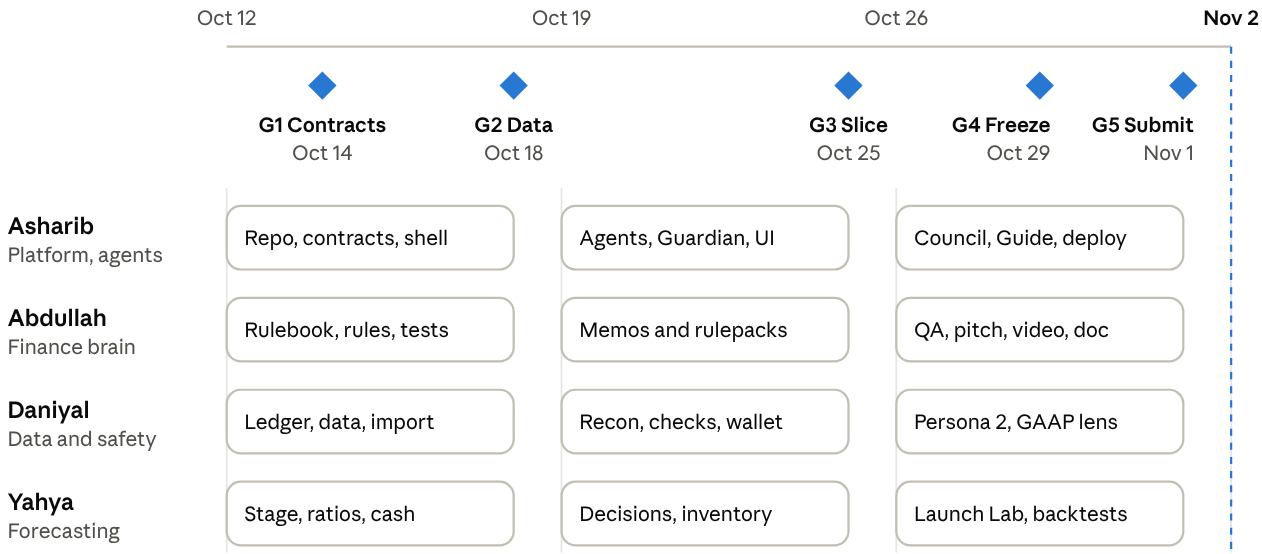

team plan · dates from this document; deadline from IEEE CIS Shenzhen

Week 1 builds the foundations everyone else depends on, week 2 builds the features, and week 3 hardens, rehearses and submits.

Gates

A gate passes only when its test is demonstrated live to the other three, not when someone says it is done.

Gate	Date	What must be true	Demonstrated by
G1 Contracts	Wed 14 Oct	Contracts frozen (API list, Proposal and Verdict objects, ledger tables); rulebook v1 and Guardian rules v1 written; generator v0 (two months of data) published; every module has a mock	Asharib and Daniyal walk through the contracts; Abdullah hands over the rulebook
G2 Data and shell	Sun 18 Oct	Generator v1 with answer key; bank, POS and bill importers load it into the ledger; web shell and engine both deployed; cash forecast v0 runs on real ledger data	Daniyal loads a fresh database from scratch in one command
G3 Vertical slice	Sun 25 Oct	One supplier bill goes in, is checked, paid through the sandbox wallet and posted to the ledger and audit log, shown on the briefing; reconciliation and duplicate detection catch the planted issues	Whole team runs the payment moment of the demo
G4 Feature freeze	Thu 29 Oct	Every Must item works; Should items are either working or cut; from now on only bug fixes	Abdullah's finance QA passes (task B6)
G5 Submission ready	Sun 1 Nov	Updated documentation, demo video, repository and live link all complete; backup clips recorded	Everyone checks the submission package against the organisers' rules

The organisers' deadline is Monday 2 November. Their time zone is probably China Standard Time, three hours ahead of Pakistan, so G5 on Sunday leaves a real margin; confirm the cut-off time in task S1.

Friday demos. On 16, 23 and 30 October each lane shows its work running, even if rough. A Friday demo that cannot run is treated as a slipped task.

Asharib: platform, interface and agents

Asharib's lane is the glue: if the contracts are clear and the interface is live early, the other three lanes can see their work running. The first two tasks gate everyone else.

ID	Task	Finish	Depends on	Done when	Status
A1	Monorepo with Turborepo and pnpm, CI, lint, environment template, preview deploys	Tue 13 Oct	none	A fresh clone runs web and engine locally with one command	Not started
A2	Contracts package: schemas for Proposal, Verdict, LedgerEvent and Mandate, plus the generated TypeScript client	Wed 14 Oct (G1)	D1, B2	Daniyal signs off; the package is published in the repo	Not started
A3	Web shell: login, layout, agent rail, command bar, light and dark themes	Fri 16 Oct	A1	The deployed link shows the shell running on mock data	Not started
A4	Agent runtime: Claude calls with tool use against the engine; bill extraction on Haiku first, then the Controller and Treasurer	Tue 20 Oct	A2, D2a	A photographed bill becomes a typed record with source references	Not started
A6	Guardian adversarial review on Opus and the verdict combiner that merges it with the deterministic checks	Fri 23 Oct	A2, D5	A planted bill sent to a changed bank account is blocked with reasons	Not started
A5	Briefing and approval screens: ranked cards, Guardian outcomes, approve and reject, passkey login on the phone	Sun 25 Oct (G3)	A3, A4, Y6	The payment moment of the demo works end to end on a phone browser	Not started
A7	Council mode and Guide panel (Should)	Wed 28 Oct	A4, B4	A loan-versus-equity question produces a memo; the Guide answers three scripted questions	Not started

ID	Task	Finish	Depends on	Done when	Status
A8	Integration owner: weekly integration branch, demo environment, cached answers for the scripted demo questions, installable web app on a phone	Thu 29 Oct (G4)	all lanes	The full demo runs from the live link and from cache	Not started

A6 is listed before A5 because it finishes first. If Asharib is overloaded, the first thing handed to the buddy is A7.

Abdullah: finance rulebook, tests and pitch

Abdullah decides whether the product's advice is right. Everything he writes is a rule, a test or a number someone else turns into code, so his first two tasks are what Yahya and Daniyal wait on.

ID	Task	Finish	Depends on	Done when	Status
B1	Finance rulebook v1: Stage Detector rules, decision thresholds for debt versus equity, dividend versus reinvestment and capital spending, priorities per stage, written as YAML plus a one-page table	Wed 14 Oct (G1)	none	Yahya can implement every rule without asking a question	Not started
B2	Guardian rules v1: finalise the twelve draft rules in the blueprint (thresholds and outcomes) and the default mandate for each agent	Wed 14 Oct (G1)	none	Daniyal and Asharib can code every rule; mandates are in the contracts package	Not started
B3	Test scenarios: twelve planted-issue scenarios with expected verdicts, written with Daniyal for the generator's answer key	Sat 17 Oct	B2, D2a	Each scenario has a data spec, an expected outcome and a rule ID	Not started

ID	Task	Finish	Depends on	Done when	Status
B4	Gold-standard memos: three hand-written decision memos (debt versus equity, dividend, new product) and a scoring rubric	Thu 22 Oct	B1, D2	The rubric scores a memo out of 10 on ratios, direction and stated assumptions; Asharib tunes prompts against it	Not started
B5	Framework rulepack content: IFRS, IFRS for SMEs and US GAAP differences for inventory, property and equipment, leases and development costs, each row citing the standard; CAS presentation mapping (Could)	Sat 24 Oct	none	Tables ready for Daniyal to encode in D8	Not started
B6	Finance QA: recompute every number shown in the demo by hand or in a spreadsheet and sign off	Thu 29 Oct (G4)	all numeric tasks	A signed list with source and match for each number	Not started
B7	Pitch and video: narration script timed to five minutes, storyboard, list of backup clips	Fri 30 Oct	B4	Script rehearsed twice; video recorded	Not started
B8	Submission document: update the Fiona documentation with real screens and measured results	Sun 1 Nov (G5)	A8, Y7	Every claim in the document matches what the demo shows	Not started

If Abdullah writes code, B1 and B2 become working modules instead of files; the rest is unchanged.

Daniyal: data, ledger and safety

Daniyal's lane is the critical path. D1 to D3 are what the other three lanes build against, so they come first and nothing else starts before D2a is published.

ID	Task	Finish	Depends on	Done when	Status
D1	Ledger schema: migrations for the tables in the blueprint, row-level security, a seed script	Wed 14 Oct (G1)	none	One command builds an empty database, and Asharib can generate types from it	Not started
D2a	Generator v0: two months of data for the Karachi apparel retailer in the agreed file formats	Wed 14 Oct (G1)	D1	Everyone has fixture files to mock against	Not started
D2	Generator v1: 24 months, planted issues, and an answer key listing every planted issue with its row IDs	Sat 17 Oct	B3	The same seed rebuilds identical data; the answer key covers all twelve scenarios	Not started
D3	Importers: bank CSV, POS CSV and extracted bills into canonical ledger events	Sun 18 Oct (G2)	D1, D2	One command loads the full dataset into a fresh database	Not started
D4	Reconciliation matcher (exact, rule-based and one-to-many passes) and the duplicate detector	Thu 22 Oct	D3, B3	Every planted duplicate is caught; match rate against the answer key is reported	Not started
D5	Guardian deterministic checks (policy, evidence, arithmetic) and the mandate table	Fri 23 Oct	B2, A2	Each of the twelve rules has a passing test built from its scenario	Not started
D6	Agent-wallet sandbox: simulated account with caps, payee allow-list and cooling-off, payments only with a cleared verdict, hash-chained audit log	Sun 25 Oct (G3)	D5	A payment with no cleared verdict is refused, and an edited log entry is detected	Not started
D7	Second persona: Shenzhen distributor in CNY, with a tenant switch (Should)	Tue 27 Oct	D2	Switching tenant shows a different business with different data	Not started
D8	Framework lens: encode Abdullah's IFRS and US GAAP tables for inventory and leases (Should)	Wed 28 Oct	B5	One ledger shows two inventory valuations by framework and the difference between them	Not started

If Daniyal falls behind, D7 and D8 are cut first, and Asharib, as his pair, takes any part of D5 that is blocked.

Yahya: forecasting, decisions and Launch Lab

Yahya turns the ledger into numbers that drive decisions. He builds against Daniyal's generator v0 files until the real database is ready at G2, then switches over without changing the code that calls it.

ID	Task	Finish	Depends on	Done when	Status
Y2	Stage Detector and ratio library (leverage, interest cover, debt-service coverage, margins) implementing Abdullah's rulebook	Sat 17 Oct	B1, D2a	Returns the stage and its working for the Karachi retailer, matching Abdullah's hand calculation	Not started
Y1	13-week cash forecast from ledger events and open invoices and bills, with a flag for the first week below the owner's buffer	Sun 18 Oct (G2)	D2a, then D3	The forecast runs on the generator data and flags the planted cash dip	Not started
Y3	Inventory analytics: ABC–XYZ classes, reorder points, dead stock, margin per item	Thu 22 Oct	D3	The planted slow movers are listed with the cash each ties up	Not started
Y4	Decision calculators: debt versus equity (coverage and runway under each), dividend versus reinvestment, NPV, IRR and payback	Fri 23 Oct	Y2, B1	Each returns its numbers plus the inputs and thresholds used, so Abdullah can recompute them	Not started
Y6	Findings feed: forecast and inventory findings as typed items ranked by money at stake, for the briefing	Fri 23 Oct	Y1, Y3	Asharib's briefing endpoint can include the feed with no extra code	Not started

ID	Task	Finish	Depends on	Done when	Status
Y5	Launch Lab v1: inputs, demand proxies from a cached and labelled dataset plus the firm's own sales, Chronos-2 forecast, Monte Carlo low, base and high cases, break-even and payback	Tue 27 Oct	Y1, Y3	The winter-shawl scenario returns a break-even month and the probability of breaking even in the owner's horizon	Not started
Y7	Evaluation: backtest the cash forecast and Launch Lab against the generator's known truth and write up the errors	Wed 28 Oct	Y1, Y5, D2	A table of error figures ready for the submission document	Not started

For the demo, demand signals come from a cached, clearly labelled dataset, so the result is repeatable on stage; live trend pulls are a Could item. If Yahya falls behind, the Monte Carlo part of Y5 shrinks to a simple low, base and high range, and Abdullah, as his pair, checks Y2 and Y4 outputs.

Shared tasks and routines

ID	Task	Owner	Finish	Done when	Status
S1	Read the organisers' rules: confirm eligibility for a Pakistan-based team, the submission format, video length and language, and the exact cut-off time	Abdullah	Wed 14 Oct	A one-paragraph summary posted to the team; anything that changes scope is raised the same day	Not started
S2	Shared accounts and secrets: Supabase, Vercel, Fly.io, a Claude API key with a spending cap, and a shared password manager	Asharib	Tue 13 Oct	All four can deploy and call the API without sharing keys in chat	Not started
S3	Two timed run-throughs of the five-minute demo	All	Thu 29 Oct and Sat 31 Oct	Both finish inside five minutes with the backup clips ready	Not started
S4	Submission package check against the organisers' rules	All	Sun 1 Nov (G5)	A checklist ticked by all four before anything is uploaded	Not started

Routines

- **Daily standup, 15 minutes.** Three lines each: done since yesterday, doing today, blocked on. Proposed time: 9:00 pm Pakistan time after classes; if someone cannot attend, they post the three lines in the group chat instead.
- **Friday demo, 16, 23 and 30 October.** Each lane shows its work running. The demo is the status report.
- **Pull requests.** Small, reviewed by someone else within 24 hours, merged to the integration branch only if the build is green.
- **Decisions.** Anything that changes a contract or a date goes into the open-decisions table in the blueprint, with an owner and a date.

Cut order

If a gate slips by more than a day, the next item on this list is cut at once, without a debate. Deciding the order now means nobody argues about it when tired.

1. D8 framework lens, and the CAS mapping in B5
2. The Guide panel in A7

3. D7 second persona, replaced by a recorded clip of the Shenzhen switch
4. Council mode in A7, replaced by a single memo from the CFO Strategist
5. The Monte Carlo part of Y5, replaced by a plain low, base and high range
6. Phone passkey approval in A5, replaced by approval in a desktop browser
7. Live Launch Lab in Y5, replaced by a recorded run (last resort)

Never cut: A2, A4, A5, A6, A8, B1, B2, B6, B7, D1 to D6, Y1, Y2 and Y4. Without them there is no vertical slice, and the demo's central claim, that the AI is checked before it acts, cannot be shown.

Risks and assumptions

Assumptions to confirm this week. The plan is sized on these; if one is wrong, the dates change, so each person should confirm or correct theirs by Wednesday.

Assumption	Why it matters	Who confirms
About 15 focused hours a week each	The task counts and dates are sized to it; at 8 hours, the Should items go	Everyone
Abdullah is strongest in finance rather than code	His lane is rules, tests and content; if he codes, he takes Y2	Abdullah
Daniyal and Yahya are comfortable in Python and SQL	Both lanes are mostly Python	Daniyal, Yahya
Free tiers of Supabase, Vercel and Fly.io are enough	A paid plan would need a card and a budget decision	Asharib
No exams or deadlines clash with the gates	Each person adds their own dates to a comment on this line	Everyone
The team is eligible under the final rules	Pakistan is not an APEC economy; this is task S1	Abdullah

Risks

Risk	Early warning	Response
Daniyal's lane becomes the bottleneck	D2a is not published by Wed 14 Oct	The others build on hand-made fixtures; Asharib takes the blocked part of D5
Contracts change after G1	A pull request edits the contracts package	Only through the open-decisions table, with both signatories
Claude calls cost more or run slower than planned	Spend or latency in the first agent test	Haiku for extraction, Sonnet for reasoning, cached answers for the demo (A8)
The demo fails on the day	Any moment fails in a run-through	Pre-loaded data, recorded clips for all seven moments, cached answers
Someone is out for several days	A missed standup with no message	The pair takes over the next task in that lane
Scope creep	A new idea appears after G1	It goes to the parked list in the blueprint, not into the sprint
